ID	Task Mode	Task Name	Duration	Start	Finish
1		Respond to Academy funding decision by DFE (EFA)	14 days	Mon 14/12/15	Thu 31/12/15
2		Finalise Partner requirements for final Business Case	23 days	Tue 01/12/15	Thu 31/12/15
3		Renewables/district heating feasibility study for West Mildenhall completed			Fri 12/02/16
4		Consult and adopt Hub Development Brief	72 days	Mon 08/02/16	Tue 17/05/16
5		Partners update business plan and identify partnership agreements needed			Mon 29/02/16
6		Consider Hub management model	20 days	Mon 04/01/16	Fri 29/01/16
7		Concept design produced	20 days	Mon 15/02/16	Fri 11/03/16
8		Appoint design team	25 days	Mon 29/02/16	Fri 01/04/16
9		**Developed Design**	**219 days?**	**Tue 01/03/16**	**Fri 30/12/16**
10		Complete Pre-Planning Application Work:	65 days	Mon 04/04/16	Fri 01/07/16
11		Start discussions with waste pipe owner	45 days	Tue 01/03/16	Sat 30/04/16
12		Commission Transport Study for solution to war memorial junction	88 days	Tue 01/03/16	Thu 30/06/16
13		Ecology Survey	43 days	Fri 01/04/16	Tue 31/05/16
14		Archaeological Trenching	20 days	Mon 04/04/16	Fri 29/04/16
15		Environmental Impact Assessment	65 days	Mon 04/04/16	Fri 01/07/16
16		Ongoing consultation prior to planning submission	130 days	Mon 04/04/16	Fri 30/09/16
17		Prepare and adopt financial business case to reflect funding decisions and phasing requirements	88 days	Wed 01/06/16	Fri 30/09/16
18		Planning Submission by			Mon 03/10/16
19		Planning Consent Achieved by			Fri 30/12/16
20		**Technical Design**			
21		Run Contractor Procurement	69 days	Mon 29/05/17	Thu 31/08/17
22		Contractor Mobilisation	15 days	Mon 04/09/17	Fri 22/09/17
23		**Construction**	**325 days**	**Mon 25/09/17**	**Fri 21/12/18**
24		Discharge Planning Conditions - Dates TBC			
25		Commence Leisure Facilities, office space, other public sector uses and shared infrastructure	325 days	Mon 25/09/17	Fri 21/12/18
26		Commence exclusive Academy elements	260 days	Mon 25/09/17	Fri 21/09/18
27		Town Centre Junction Improvements made	46 days	Mon 30/10/17	Sun 31/12/17
28		Phase 1 in use (leisure and other public sector uses)			Fri 21/12/18

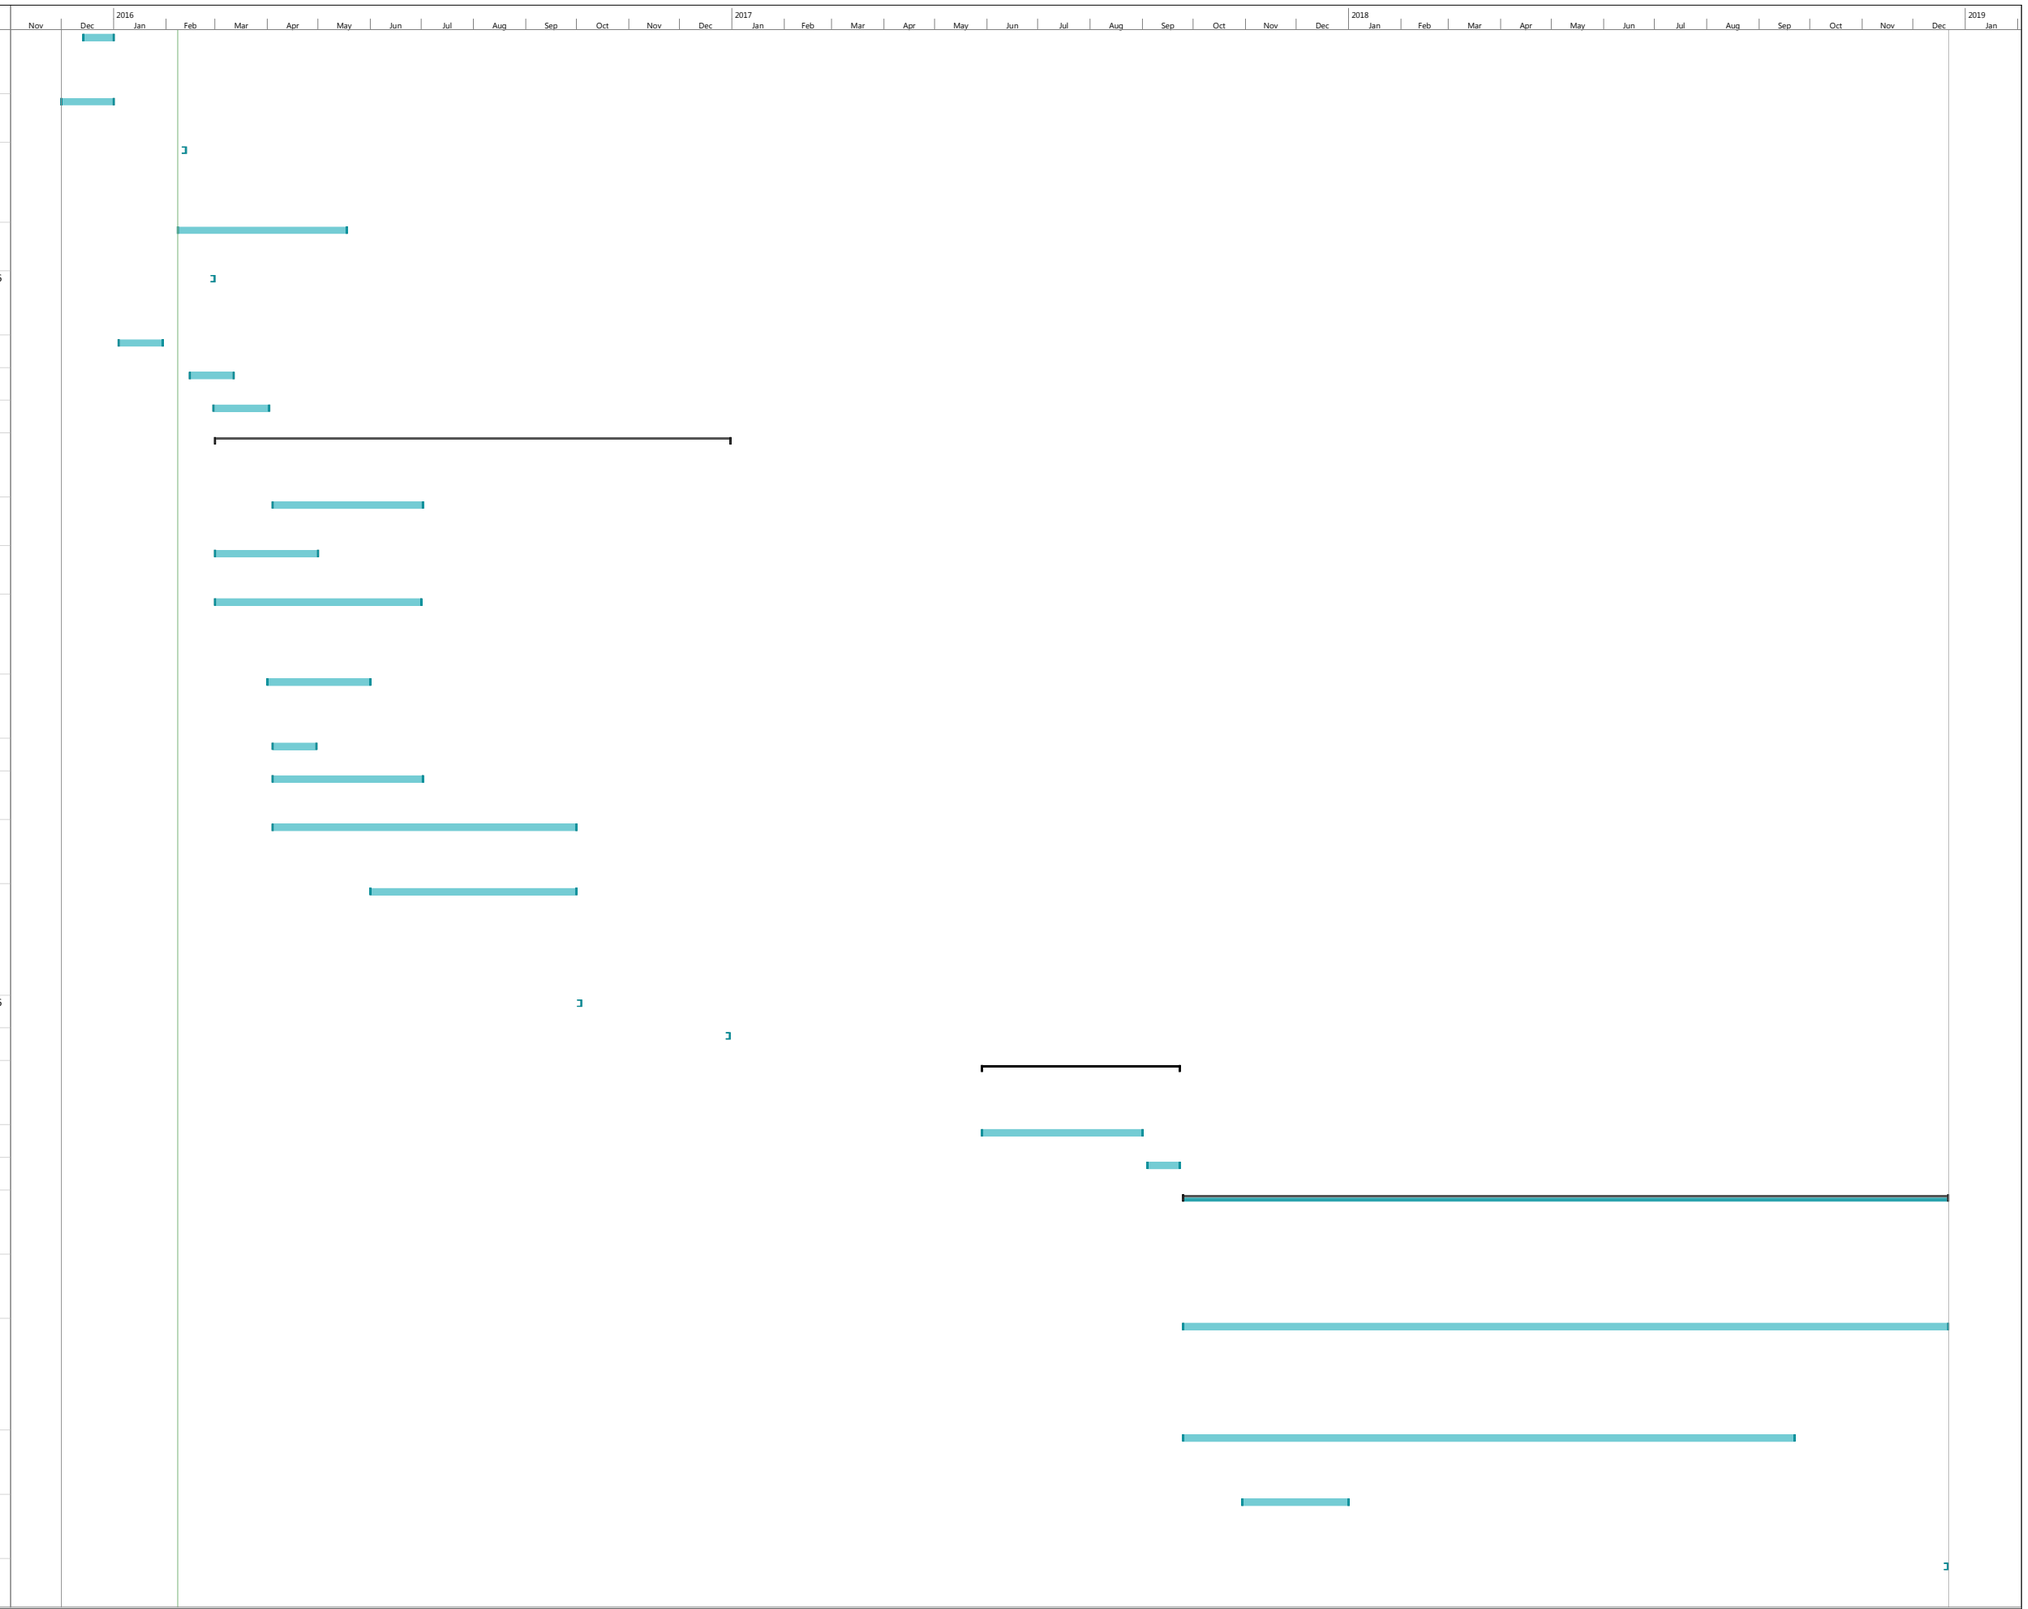

Project: 13-0512 - Publications
Date: Mon 08/02/16

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
